

NORTH COAST PIPELINES & HAZELMERE SUPPLY INFRASTRUCTURE

Strategy Steering Committee – Meeting 4, 14 March 2012
Implementation and Maintenance of the Water Reconciliation Strategy for the KZN Metropolitan Areas




Progress to date

- Honolulu to Mvoti Balancing Reservoir Pipeline
 - Pipeline contract was completed in October 2010
 - The construction of the pipe bridge is approximately 85% complete
 - The programme for the booster pump station still to be determined once the land issue is resolved

Progress to date

- Hazelmere Raw water Pipeline
 - Construction tender is being evaluated
- Hazelmere WTP Upgrade
 - Construction tender has been advertised
- Hazelmere to Bifurcation Pipeline & Pump Station
 - Contractor appointed to construct the pipeline. Pipe has been ordered.
- Environmental Authorisation obtained

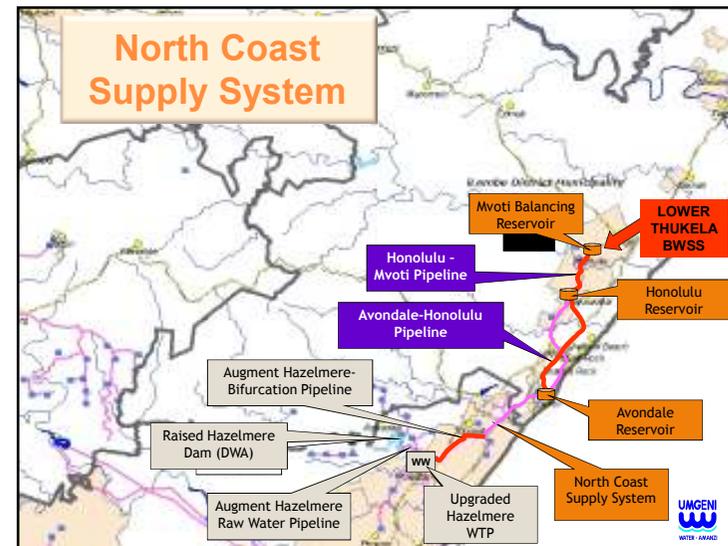

Way forward

- Honolulu to Mvoti Balancing Reservoir Pipeline
 - Construction of the pipe bridge is practically complete
 - Resolve land issues and completed pump station (by ?)
- Hazelmere supply infrastructure
 - Complete the upgrade of:
 - Raw water pipeline from dam to waterworks (2013)
 - Upgrade of Hazelmere WTP to 75MI/day (December 2013)
 - Upgrade Hazelmere to Bifurcation Pipeline and Pump Station (December 2012)
