


NORTH COAST PIPELINE AND HAZEMERE SUPPLY INFRASTRUCTURE



11 September 2012



Strategy Steering Committee – Meeting 5
Implementation and Maintenance of the Water Reconciliation Strategy for the KZN Metropolitan Areas

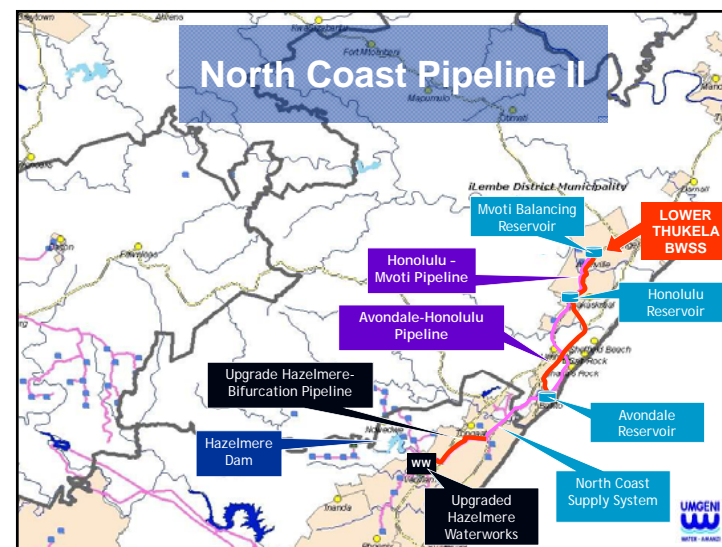

Progress to date

- Avondale to Honolulu Pipeline completed in November 2009
- Honolulu to Mvoti Balancing Reservoir Pipeline
 - Pipeline contract was completed in October 2010
 - The construction of the pipe bridge has been completed
 - Approved received from Minister to expropriate the land for the pump station received in August 2012
- Hazelmere Raw water Pipeline
 - Construction contract was awarded in June 2012
 - Contract withdrawn in July 2012 as they were liquidated
 - New contractor appointed in July 2012
- Hazelmere WTP Upgrade
 - Construction contract awarded end August 2012
- Hazelmere to Bifurcation Pipeline & Pump Station
 - Construction contract awarded in February 2012 and construction currently underway
 - Tender documentation for the pump station is being compiled.

Way forward

- Honolulu to Mvoti Balancing Reservoir Pipeline
 - Negotiations with Contractor are underway as to when construction of the pump station can commence
- Hazelmere supply infrastructure - Complete the upgrade of:
 - Raw water pipeline from dam to waterworks (March 2013)
 - Upgrade of Hazelmere WTP to 75ML/day (February 2014)
 - Upgrade Hazelmere to Bifurcation Pipeline and Pump Station (March 2013/ May 2014)
